Planning Chart for: Plot 1
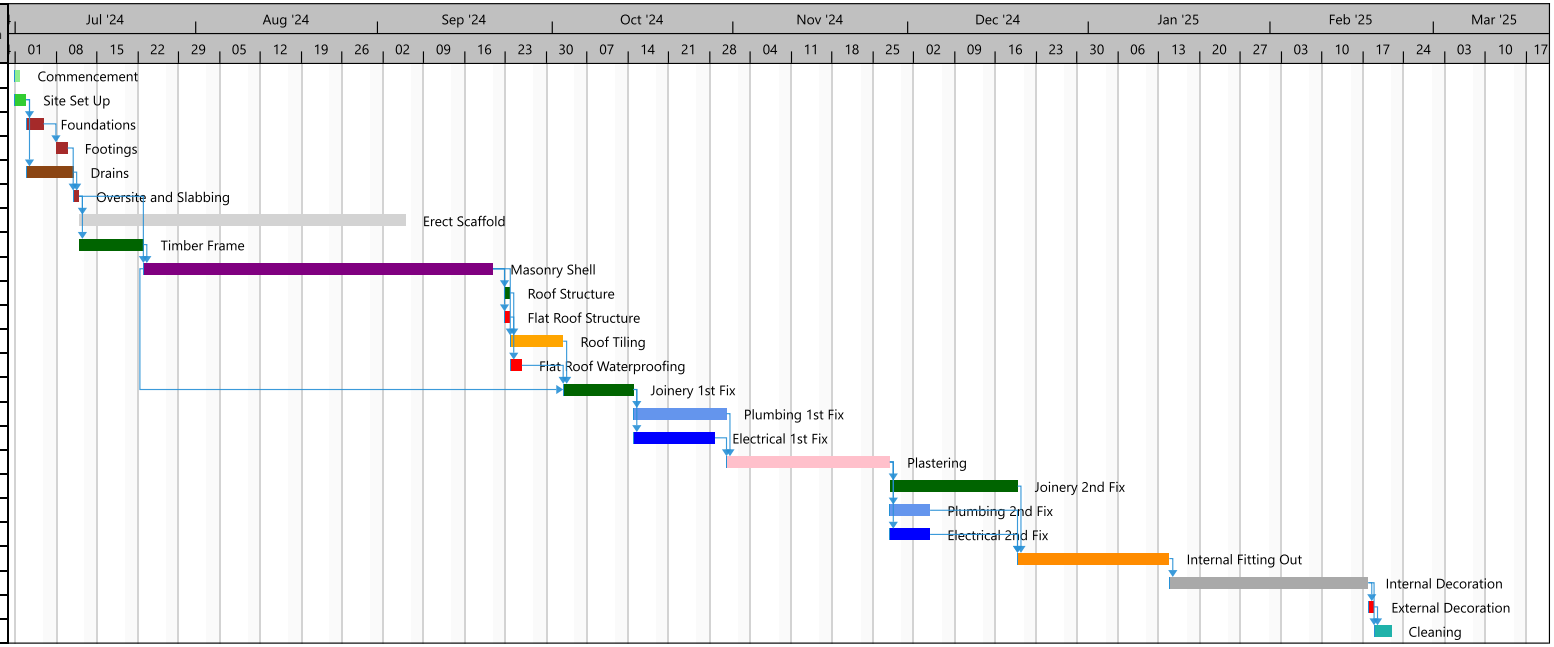
Name	Start	Duration
Commencement	01/07/2024	1d
Site Set Up	01/07/2024	2d
Foundations	03/07/2024	3d
Footings	08/07/2024	2d
Drains	03/07/2024	6d
Oversite and Slabbing	11/07/2024	1d
Erect Scaffold	12/07/2024	40d
Timber Frame	12/07/2024	7d
Masonry Shell	23/07/2024	44d
Roof Structure	23/09/2024	1d
Flat Roof Structure	23/09/2024	1d
Roof Tiling	24/09/2024	7d
Flat Roof Waterproofi...	24/09/2024	2d
Joinery 1st Fix	03/10/2024	8d
Plumbing 1st Fix	15/10/2024	12d
Electrical 1st Fix	15/10/2024	10d
Plastering	31/10/2024	20d
Joinery 2nd Fix	28/11/2024	16d
Plumbing 2nd Fix	28/11/2024	5d
Electrical 2nd Fix	28/11/2024	5d
Internal Fitting Out	20/12/2024	18d
Internal Decoration	15/01/2025	24d
External Decoration	18/02/2025	1d
Cleaning	19/02/2025	3d
